

Weather Assessment Executive Report


YHO_FEM2 (base 2030_42 locations)_Rev.2K_3

Planning year	Total positions	Completed scenarios	Selected P0	Exact P0
2030	42	44/45	114.496 days	114.496 days

Report basis	Value
Project / scenario	YHO_FEM2 (base 2030_42 locations)_Rev.2K_3
Planning start	2030-04-01
Simulation timestep	0.250 h
Detailed results basis	P0 (no weather)
Selected detail hindcast year	Not applicable - P0
Weather datasets	OFFSHORE: FM2_WF_weathe_reconciled_Rev.0.csv; PORT: FM2_WF_weathe_reconciled_Rev.0.csv; TRANSIT: FM2_WF_weathe_reconciled_Rev.0.csv
Document status	Review output

This report follows the detailed-results basis selected in Campaign settings (P0 (no weather)). A cycle-grouped Microsoft Project XML schedule for the same selected basis is available separately from the app export page.

1. Executive summary




Executive observations
- The assessment includes 44 completed hindcast scenarios from 45 simulated start years.
- The selected detailed output is deterministic P0 (114.496 d) with zero weather downtime.
- P50, P75 and P90 durations are statistical percentile results across completed hindcast simulations.
- P0 is a continuous no-weather programme and has no representative hindcast year.


Planning scenario	Statistical duration [days]	Representative hindcast year	Representative duration [days]	Difference [days]
P50	169.198	1984	169.156	0.042
P75	179.031	2005	178.990	0.042
P90	190.864	1997	191.729	0.866

2. Overall campaign profile

Campaign duration by scenario

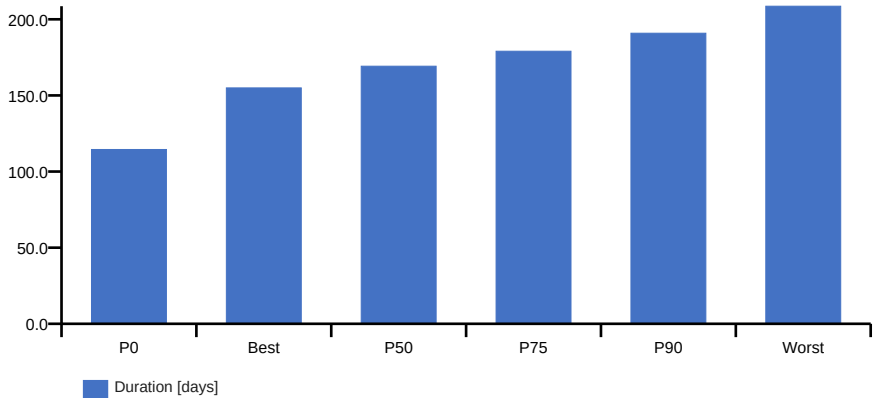

Position completion profile

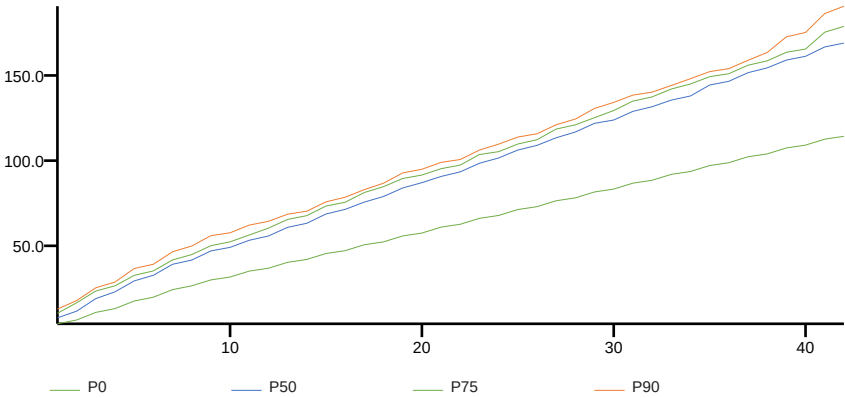


Position	P0 [days]	P50 [days]	P75 [days]	P90 [days]
1	4.227	7.724	10.359	12.835
10	31.679	49.094	52.331	57.641
21	60.967	90.719	95.281	98.972
32	88.467	131.630	137.396	140.219
42	114.279	168.979	178.812	190.645
Campaign complete	114.496	169.198	179.031	190.864


Position completion can precede full campaign completion because Type 3 close-out activities may remain after the final position milestone.

3. Monthly planning profile

Positions completed in the month

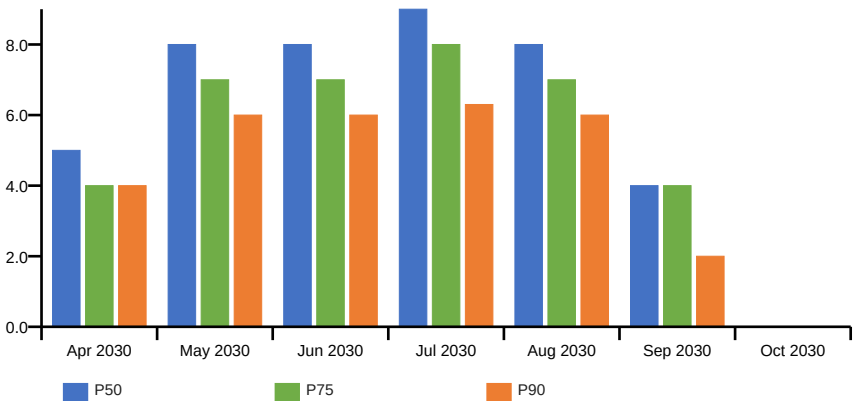

Cumulative positions completed

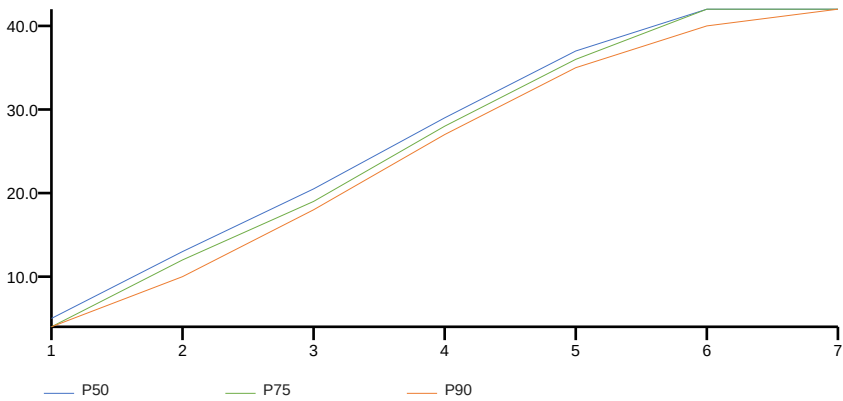

Month	P50 positions	P75 positions	P90 positions	P50 cumulative	P75 cumulative	P90 cumulative
Apr 2030	5.000	4.000	4.000	5.000	4.000	4.000
May 2030	8.000	7.000	6.000	13.000	12.000	10.000
Jun 2030	8.000	7.000	6.000	20.500	19.000	18.000
Jul 2030	9.000	8.000	6.300	29.000	28.000	27.000
Aug 2030	8.000	7.000	6.000	37.000	36.000	35.000
Sep 2030	4.000	4.000	2.000	42.000	42.000	40.000
Oct 2030	0.000	0.000	0.000	42.000	42.000	42.000



4. Representative scenarios and planning milestones

Planning scenario	Statistical duration [days]	Estimated finish	Representative hindcast year	Representative duration [days]	Difference [days]
P50	169.198	17 Sep 2030	1984	169.156	0.042
P75	179.031	27 Sep 2030	2005	178.990	0.042
P90	190.864	08 Oct 2030	1997	191.729	0.866

Position	P50 date	P75 date	P90 date	P50 elapsed [days]	P75 elapsed [days]	P90 elapsed [days]
1	08 Apr 2030	11 Apr 2030	13 Apr 2030	7.724	10.359	12.835
10	20 May 2030	23 May 2030	28 May 2030	49.094	52.331	57.641
21	30 Jun 2030	05 Jul 2030	08 Jul 2030	90.719	95.281	98.972
32	10 Aug 2030	16 Aug 2030	19 Aug 2030	131.630	137.396	140.219
42	16 Sep 2030	26 Sep 2030	08 Oct 2030	168.979	178.812	190.645

Representative-year detail does not replace the statistical percentile result. It provides a complete historical schedule and detailed downtime trace for review.

5. Planning workability and downtime

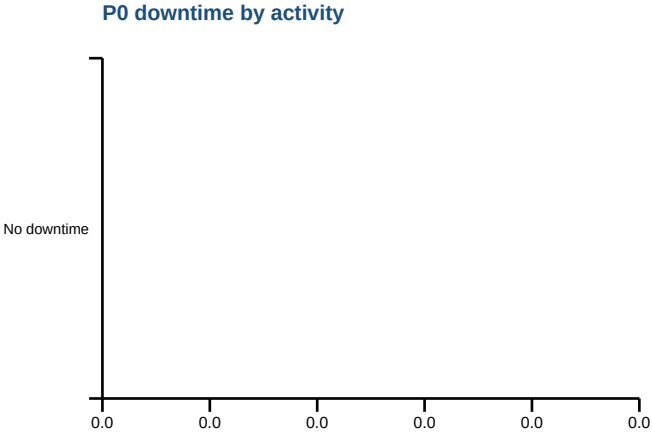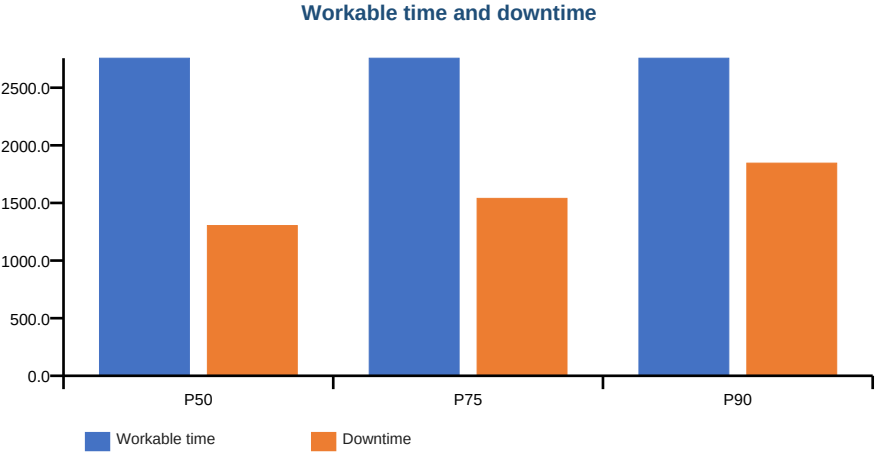

Scenario	Representative year	Statistical duration [days]	Representative duration [days]	Workable [h]	Downtime [h]	Downtime [%]
P50	1984	169.198	169.156	2,756.000	1,303.750	32.114%
P75	2005	179.031	178.990	2,756.000	1,539.750	35.844%
P90	1997	190.864	191.729	2,756.000	1,845.500	40.106%


6. P0 deterministic no-weather detail

P0 basis	Value
Exact learning-adjusted productive duration	2,747.900 h
Weather downtime	0.000 h
Weather-simulation timestep adjustment	Not applicable
Representative hindcast year	Not applicable
Execution basis	Continuous activity-to-activity schedule from the planning start

Metric	Value	% of campaign	Location	Working [h]	Downtime [h]	Total [h]	Downtime [%]
Workable time	2,747.900 h	100.000%	Installation port (project-specific)	0.000	0.000	0.000	0.000%
Downtime	0.000 h	0.000%	Port-Fengmiao 2 transit route	0.000	0.000	0.000	0.000%
Timestep adjustment	Not applicable	0.000%	Fengmiao 2 offshore site	2,747.900	0.000	2,747.900	0.000%

Selected detailed output is deterministic P0: exact learning-adjusted activity durations executed continuously with zero weather downtime and no weather-simulation timestep adjustment.

7. Hindcast distribution and coverage

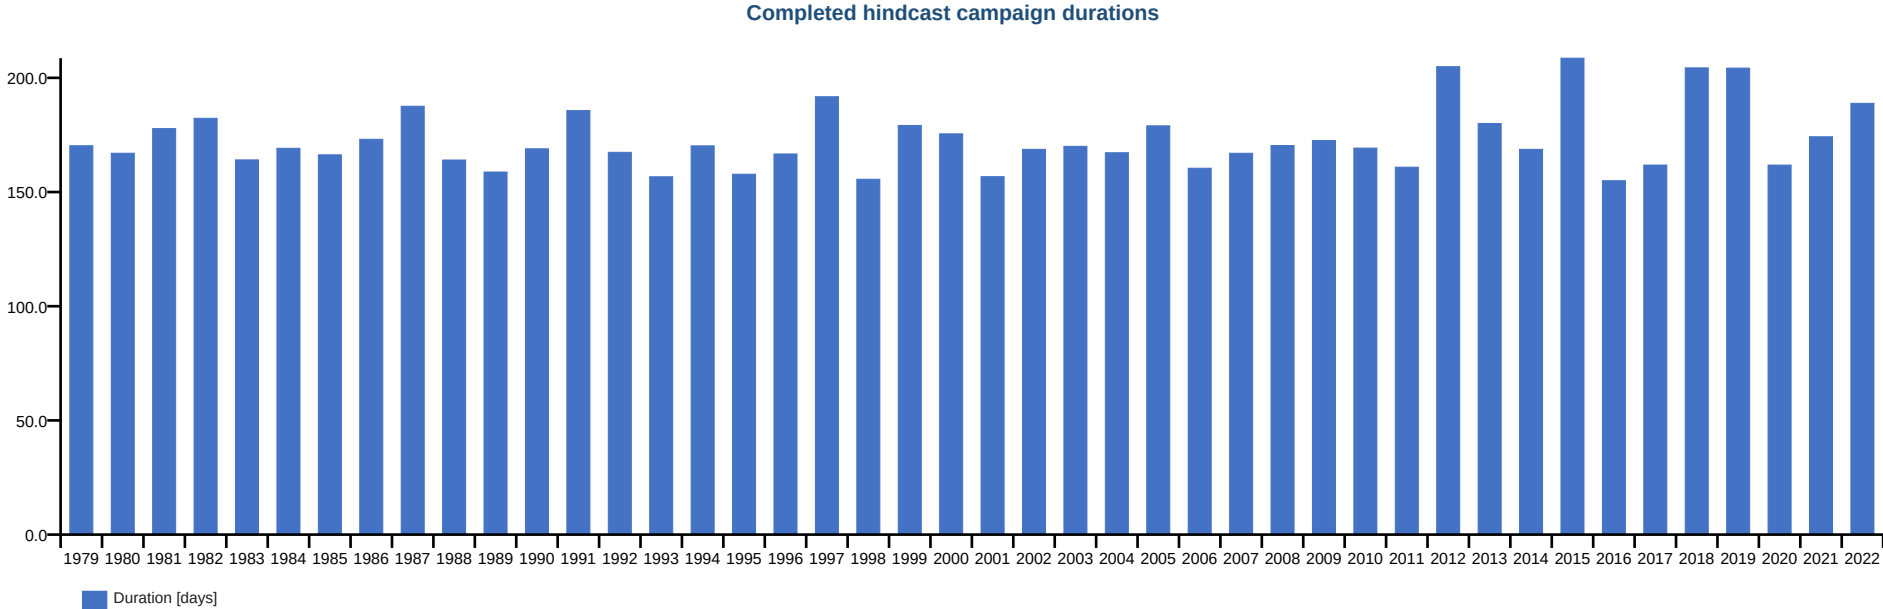

Metric	Value
Completed simulations	44
Excluded simulations	1
Campaign-year range	1979 to 2023
Mean duration	172.957 days
Median duration	169.198 days
Minimum duration	154.948 days
Maximum duration	208.604 days

Only completed hindcast simulations are included in percentile statistics. Incomplete simulations remain visible in the Excel planning-coverage output.

8. Methodology, definitions and interpretation

Term	Definition used in this report
Exact P0	Sum of exact learning-adjusted activity durations without weather delay: 2,747.900 h (114.496 d).
Timestep adjustment	Weather-simulation grid effect only. It is not applied to P0 and is reported separately from weather downtime.
Statistical P50/P75/P90	Campaign-duration and progress percentiles calculated across the completed hindcast simulations.
Representative hindcast year	A completed historical simulation selected because its total duration is closest to the statistical percentile target.
Detailed results basis	Deterministic P0, Percentile 1, 2 or 3 representative hindcast year, or one selected historical year for QA review.
Positions completed in the month	Difference between consecutive cumulative percentile position values.
Monthly downtime	Monthly weather and operational downtime percentage. It is not cumulative.
Safe-to-safe group	Consecutive activities pre-checked as one committed sequence from one safe state to the next; once started, weather waiting is not inserted between group members.
MOST_STRINGENT	Applies the most restrictive populated limits continuously across the complete committed safe-to-safe duration.
TIME_PHASED	Applies each activity's limits during its expected part of the committed safe-to-safe sequence.
Downtime cause	The actual blocking weather criterion or criterion combination, for example Hs, Tp, or Wind 10 m + Hs.
Downtime mechanism	Direct exceedance or Window pre-check. Window pre-check downtime is still attributed to the future weather criterion that blocks the required continuous window.
Data coverage exclusion	A simulation that cannot complete before the weather data ends is excluded from percentile statistics.

Source: Weather Assessment v0.10.6. Report generated 16 Sep 2026, 15:32.
